

City of Nederland Water Plant Clarifier #1

Client Name: City of Nederland

Subject: Progress Report

Created By: Trey Glasper

Westwood No.: R0043842.00

Date: 8/4/2026

Westwood

Work in Progress:

- Contractor to weld aerial bridge and have inspected by structural engineer.
- Contractor to submit remaining O&Ms
- Westwood to finalize review of Clarifier O&M and other O&Ms when submitted.
- Westwood to complete Record Drawings.

Work to be completed by next Progress Report:


- Aerial bridge completed & inspected
- O&Ms submitted, reviewed, and approved.
- Record Drawings finalized & submitted to City.
- Project Close out and City accept as final.

Updates to the Schedule:

- Completion expected to be submitted to City for review & approval in August

Project Notes / Questions:

- The substantial completion inspection was completed on June 23.

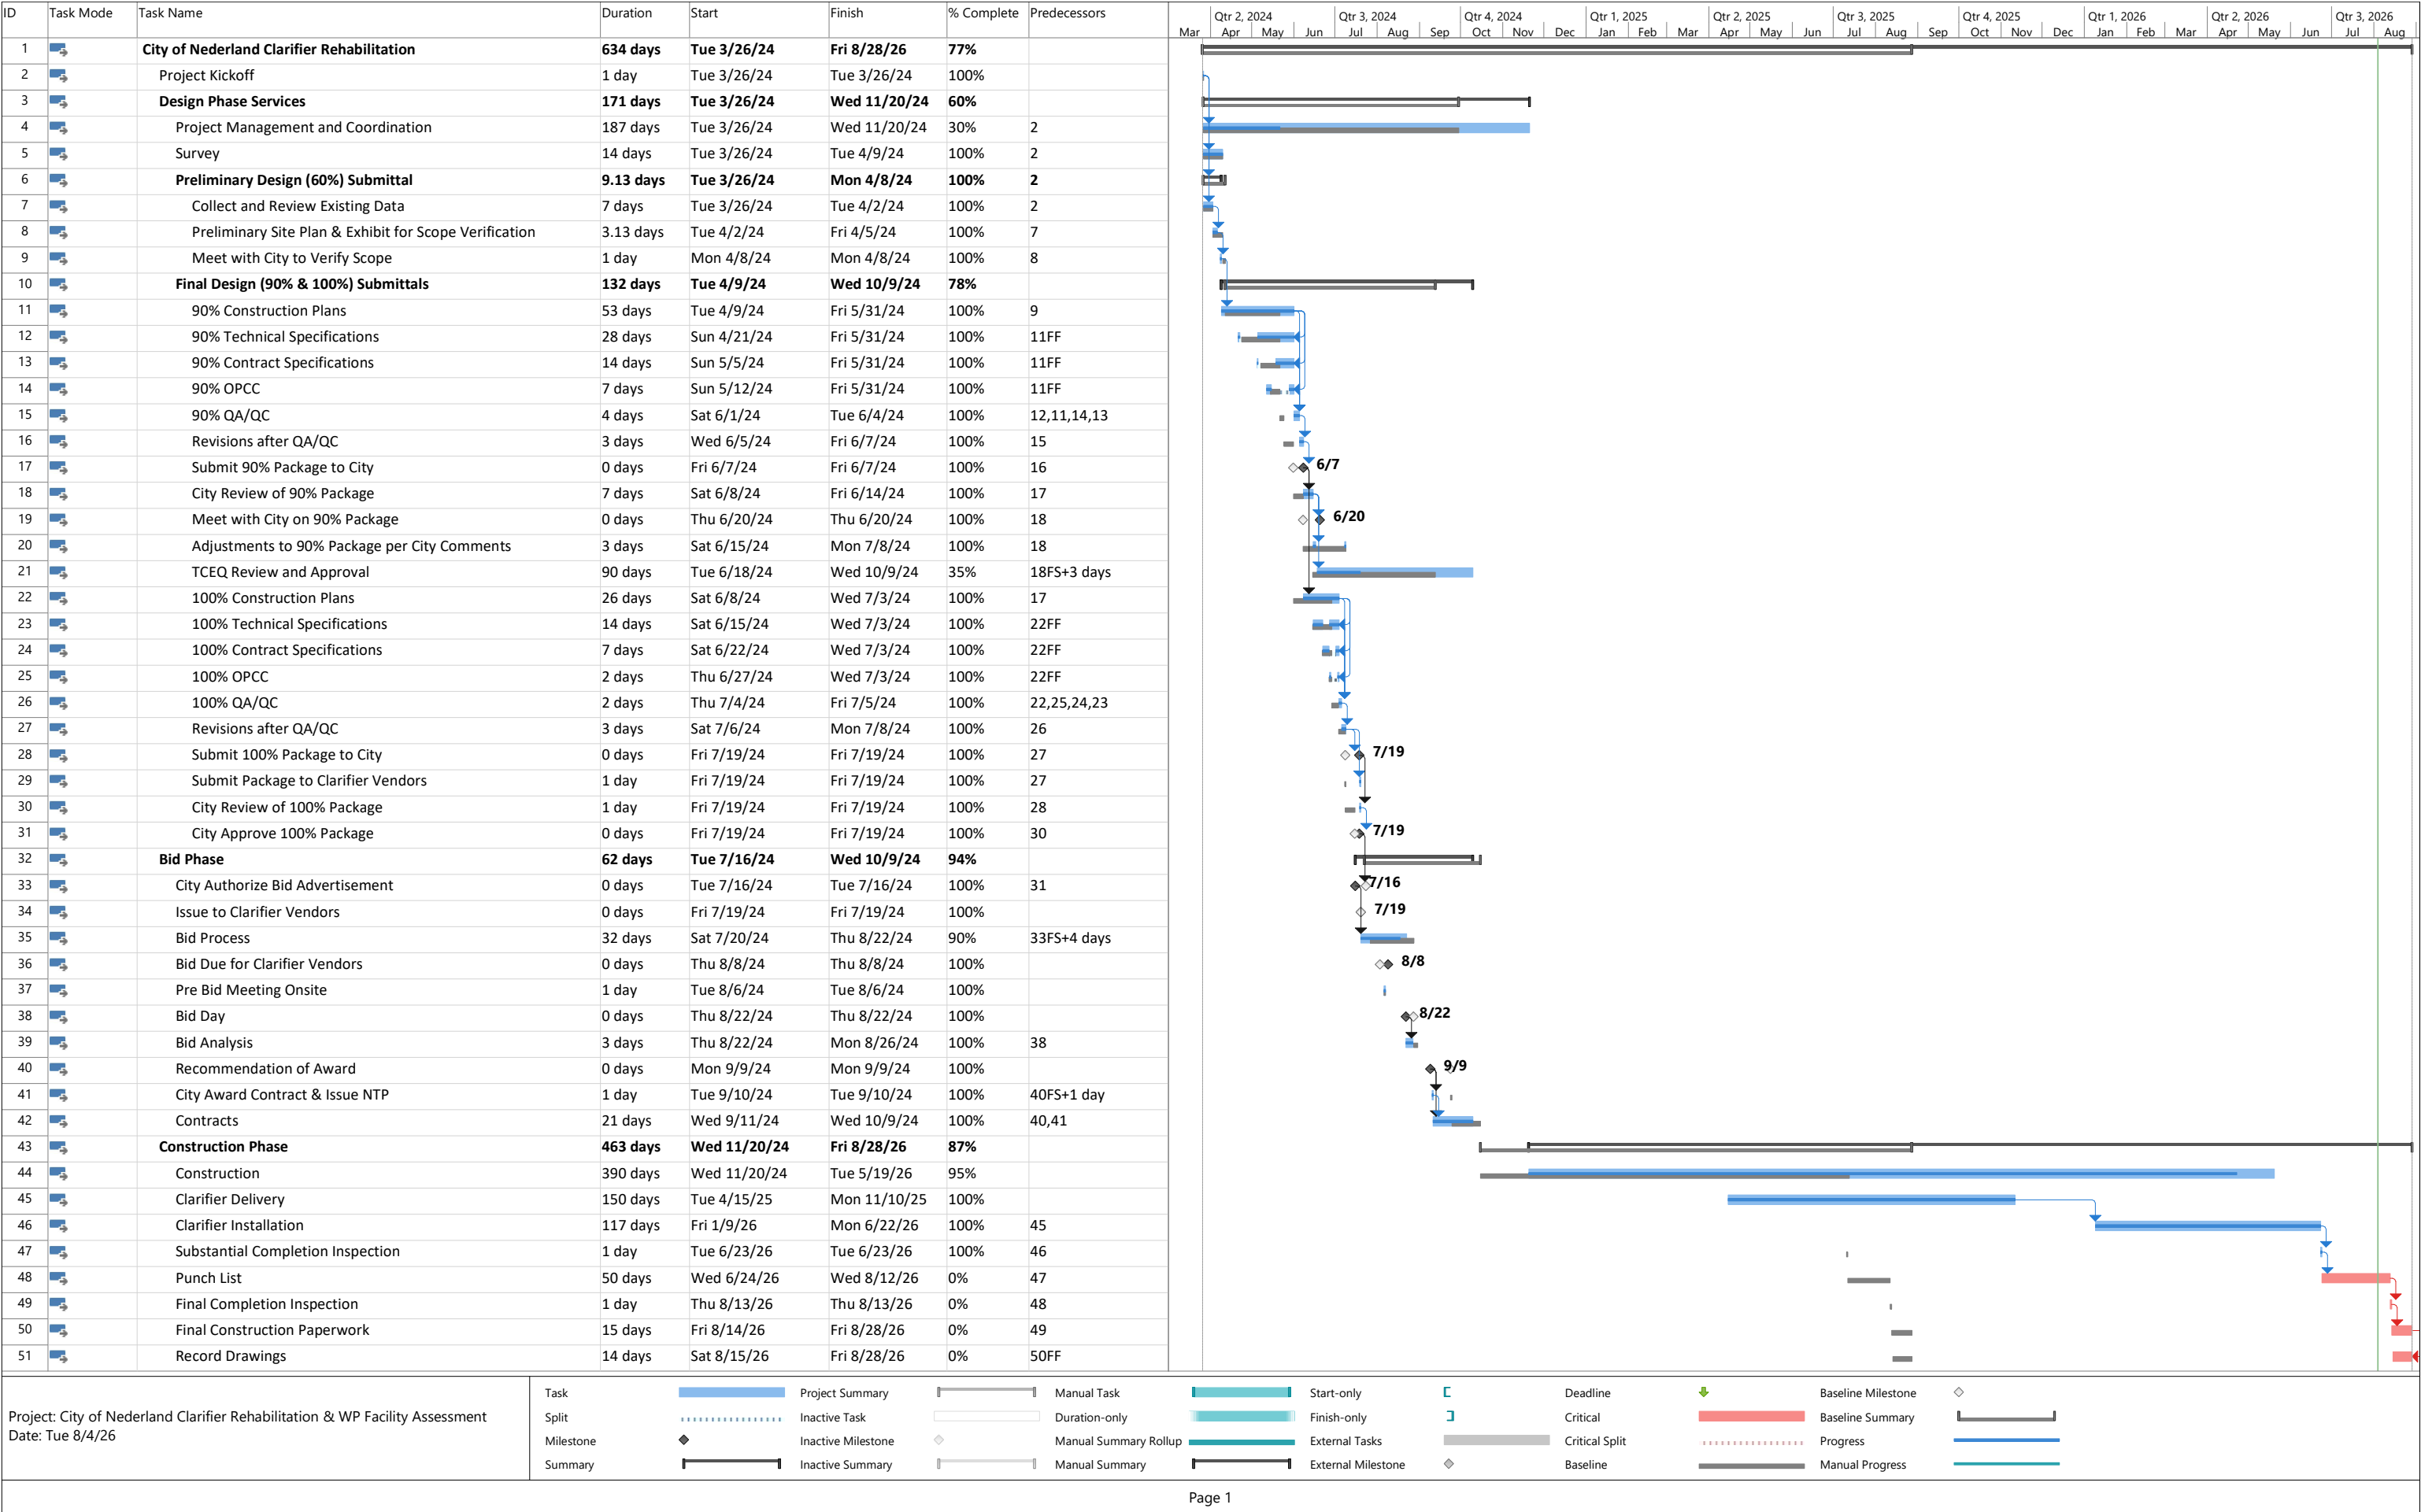

City of Nederland WWTP Centrifuge Replacement

Client Name: City of Nederland

Subject: Progress Report

Created By: Gabriela Y. Porras, PE

Westwood No.: R0043842.03

Date: 8/4/2026

Westwood

Work in Progress:

- Electrical and structural subconsultants initial sheets were received. Meetings regarding outstanding plans and outstanding questions was held with each subconsultant.
- Subconsultants are finalizing cost estimates for related work.
- Coordination with El2 and Alfa Laval to update their provided specification and plan sheets for centrifuge mounted on skid with diverter gate and polymer equipment.
- Follow up questions on pricing received from equipment suppliers. Research against previously bid similar projects in the area to evaluate various constructibility options. Coordination with structural for evaluating suitability of existing structural systems (I-beams and hoist) for getting items in/out of dewatering room.
- Coordination between subconsultants and vendors to ensure that the P&ID and required controls indicated (i.e., for pumps, centrifuges, polymer skids, diverter gate) are completely explained and covered in plans and specifications.

Work to be completed by next Progress Report:

- Final pricing and layout to be confirmed by all subconsultants on final placement and centrifuge chute locations, proposed trolley placement, proposed electrical, and proposed piping.
- Have the information from manufacturer finalized to begin procurement process. Need to final questions from electrical subs to Alfa Laval confirmed to ensure the cut sheets and specifications from vendor and the plans are reflecting the intended controls.

Updates to the Schedule:

- The schedule shows coordination with manufacturer to be completed mid-June. This was a bit delayed due to staff vacations at Alfa Laval and finding a solution for the issue of the solids discharge chute being too close to a column. Though a meeting was held with Alfa Laval recently (6/29) to discuss what has been provided and what is needed from them finalize this information for procurement. A second meeting is getting scheduled to confirm the items they provided including specifications, weights, controls, and pricing.

Project Notes / Questions:

Is there anything else the City will require besides plans and specs for procurement?



City of Nederland WWTP Facility Assessment

Client Name: City of Nederland

Subject: Progress Report

Created By: Simone King, PE

Westwood No.: R0043842.04

Date: 8/7/2026

Westwood

Work in Progress:

- Coordination with equipment suppliers and manufacturers to obtain budgetary pricing for proposed improvements is ongoing. Budgetary pricing quotes will be used to support the development of preliminary construction cost estimates included in the assessment.
- Westwood continues to develop the Facility Assessment report, including documentation of existing conditions and performance, recommendations, cost estimates, permit considerations, and project phasing. The draft Facility Assessment is on track to be submitted for the City's review by 8/21.

Work to be completed by next Progress Report:

- Continued coordination with equipment suppliers and manufacturers to confirm and refine budgetary pricing.
- Final WWTP Facility Assessment report to be submitted to the City after comments and feedback are received from the City.


Updates to the Schedule:

- Project has been delayed due to documentation of all existing conditions, recommendations, and cost estimating being more scope than originally planned for as well as receiving budgetary information from equipment vendors has been delayed and difficult.

Project Notes / Questions:

- City of Nederland WWTP operations staff to provide a site plan identifying requested lighting locations.

Project #: 0043842.04
Client: City of Nederland
Project: Wastewater Treatment Plant Facility Assessment
Date: Thu 8/6/26

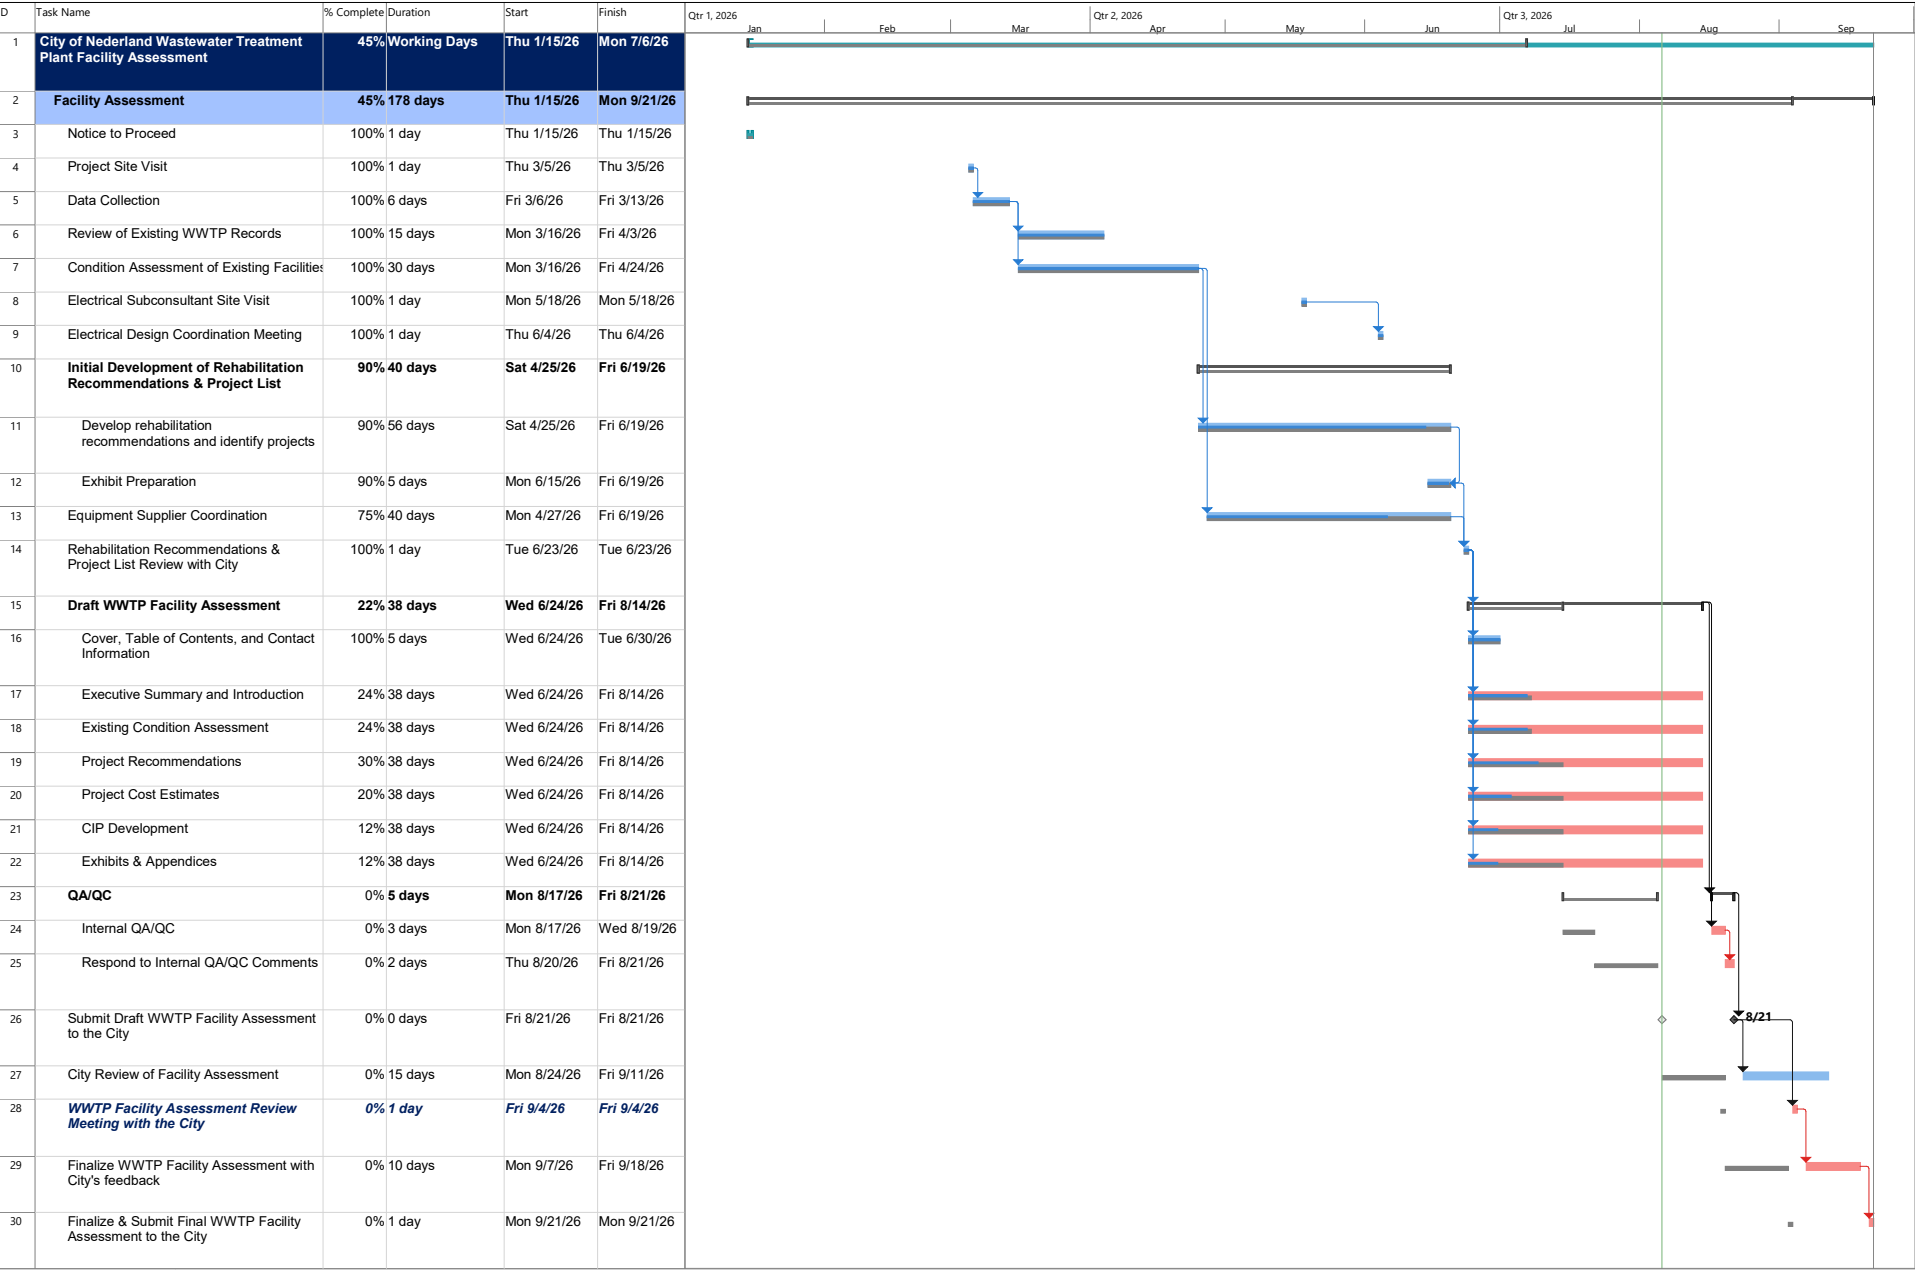

City of Nederland Lift Station Rehab

Client Name: City of Nederland

Subject: Progress Report

Created By: Jim Roberts, PE

Westwood No. R0043731.00

Date: 8/5/2026

Westwood

Work in Progress:

- Finalize pump selections for both stations
- Clarify offsite conditions at both stations
- Submit 90% plans for both lift stations

Work to be completed by next Progress Report:

- Address City comments, finalize sealed plans for bidding.
- Schedule bidding, prepare construction contracts

Updates to the Schedule:

- No changes to schedule below.

Project Notes / Questions:

- Will coordinate with City on wet well clean and inspection by AIMS.

SCHEDULE

Activity - Each Lift Station	Estimated Completion
Notice-To-Proceed	2/6/2026
Site Visit & Coord Survey & SUE	2/11/2026
Topo Survey	3/11/2026
Conceptual Design Submittal - After Survey (30%)	5/15/2026
City Review (30%)	5/29/2026
Preliminary Design Submittal (60%)	6/26/2026
City Review (60%)	7/10/2026
Bid Ready Submittal (90%)	8/7/2026
Final Client Review Complete	8/21/2026
Final Plans Complete (100%)	9/4/2026
Bidding & Award	10/30/2026
Begin Construction w/NTP	11/6/2026
Complete Construction (Estimate, per Station)	5/7/2027
Record Drawings	5/21/2027

City of Nederland Wastewater Rehab West

Client Name: City of Nederland

Subject: Progress Report

Created By: Jim Roberts, PE

Westwood No. R0069501.00

Date: 8/5/2026

Westwood

Work in Progress:

- Met and reviewed video with City and Ryan Morris on his service line issue.
- Received AI reports for Phase 1 and Phase 2 North sewer videos.
- Prepare 60% plans for Phase 2 North System
- Prepare 90% plans for Phase 1 System

Work to be completed by next Progress Report:

- Address comments on Phase 1 plans, submit final sealed plans for bidding.
- Schedule bidding for Phase 1, start construction contract documents.
- Address comments on Phase 2 North plans, submit 90% review set per schedule.
- Review Phase 2 South video, prepare plan set.

Updates to the Schedule:

- See schedule below. Blue dates are revised.
- Phase 1 90% and Phase 2 North 60% moved to 8/7/26.
- Phase 2 South 60% pushed back 1 month to 10/5/26 due to large amount of video with AI reports not yet received. It may be best to have two separate Phase 2 construction projects, very large area, will complete construction sooner with two contractors.
- Reduced construction time for Phase 1 to 6 months.

Project Notes / Questions:

SCHEDULE

Activity	PHASE 1	PHASE 2 NORTH	PHASE 2 SOUTH
Kick-off Meeting	02/11/26		
Clean & Televiser Lines - Part 1	03/01/26		
Review Video w/Client - Part 1	04/07/26	04/07/26	
Clean & Televiser Lines - Part 2, Begin Design		03/15/26	
Review Video w/Client - Part 2		04/14/26	
Clean & Televiser Lines - Part 3		05/12/26	
Review Video w/Client - Part 3		05/26/26	
Design - 60% Plans	06/23/26	08/07/26	10/05/26
City Review - 60% Plans	07/07/26	08/18/26	10/19/26
Design - 90% Plans	08/07/26	09/15/26	11/16/26
City Review - 90% Plans	08/18/26	09/29/26	11/30/26
Design - 100% Plans	09/15/26	10/16/26	12/14/26
City Review - 100% Plans	09/29/26	10/30/26	01/06/27
Bidding	11/24/26	01/30/27	03/03/27
Construction	05/28/27	01/30/28	02/29/28

City of Nederland Water Plant Clarifier #2

Client Name: City of Nederland

Subject: Progress Report

Created By: Kris Glende

Westwood No.: R0043842.02

Date: 8/4/2026

Westwood

Work in Progress:

- Survey data is being compiled into CAD
- Preliminary plan set is being reviewed by PM
- Coordination with electrical & structural subconsultant in progress.
- Clearstream is working on procurement package for mechanical components

Work to be completed by next Progress Report:

- Preliminary project plan for Operator review and agreement
- Updated project schedule
- Clarifier procurement package to be delivered to City for approval of purchasing equipment

Updates to the Schedule:

- Updated schedule will be provided 8/7.

Project Notes / Questions:

- None at this time.

City of Nederland Water Plant Chemical Feed Station Improvements

Client Name: City of Nederland

Subject: Progress Report

Created By: Kris Glende

Westwood No.: R0043842.07

Date: 8/4/2026

Westwood

Work in Progress:

- Survey data is being compiled into CAD
- Design team is working to setup drawings and move project forward
- Coordination with electrical subconsultant in progress.
- EI2 is preparing a procurement package for chemical feed equipment

Work to be completed by next Progress Report:

- Comparison of Moody Bros. and EI2 procurement packages
- Piping arrangement and operational improvements to be evaluated and determined
- Preliminary plan set to be completed and under review by PM
- Updated project schedule

Updates to the Schedule:

- Updated schedule will be provided 8/7.

Project Notes / Questions:

- None at this time.

City of Nederland Water Plant Filter Replacement

Client Name: City of Nederland

Subject: Progress Report

Created By: Kris Glende

Westwood No.: R0043842.05

Date: 8/4/2026

Westwood

Work in Progress:

- Survey data is being compiled into CAD
- Design team is working to setup drawings and move project forward
- Coordination with electrical subconsultant in progress.
- Reviewing Ovivo procurement package
- Engagement with valve and actuator vendors will be initiated ASAP

Work to be completed by next Progress Report:

- Piping arrangement and operational improvements to be evaluated and determined
- Preliminary plan set to be completed and under review by PM
- Draft construction sequencing will be prepared and reviewed with Operator
- Updated project schedule

Updates to the Schedule:

- Updated schedule will be provided 8/7.

Project Notes / Questions:

- None at this time.
