

City of Nederland Water Plant Clarifier #1

Client Name: City of Nederland

Subject: Progress Report

Created By: Trey Glasper

Westwood No.: R0043842.00

Date: 7/1/2026

Westwood

Work in Progress:

- Contractor to address substantial completion punch list items

Work to be completed by next Progress Report:


- Confirm all punch list items addressed
- Contractor to provide all finalizing paperwork (affidavits, final pay app, O&Ms, red line drawings)

Updates to the Schedule:

- Completion expected to be submitted to City for review & approval in July

Project Notes / Questions:

- The substantial completion inspection was completed on June 23.

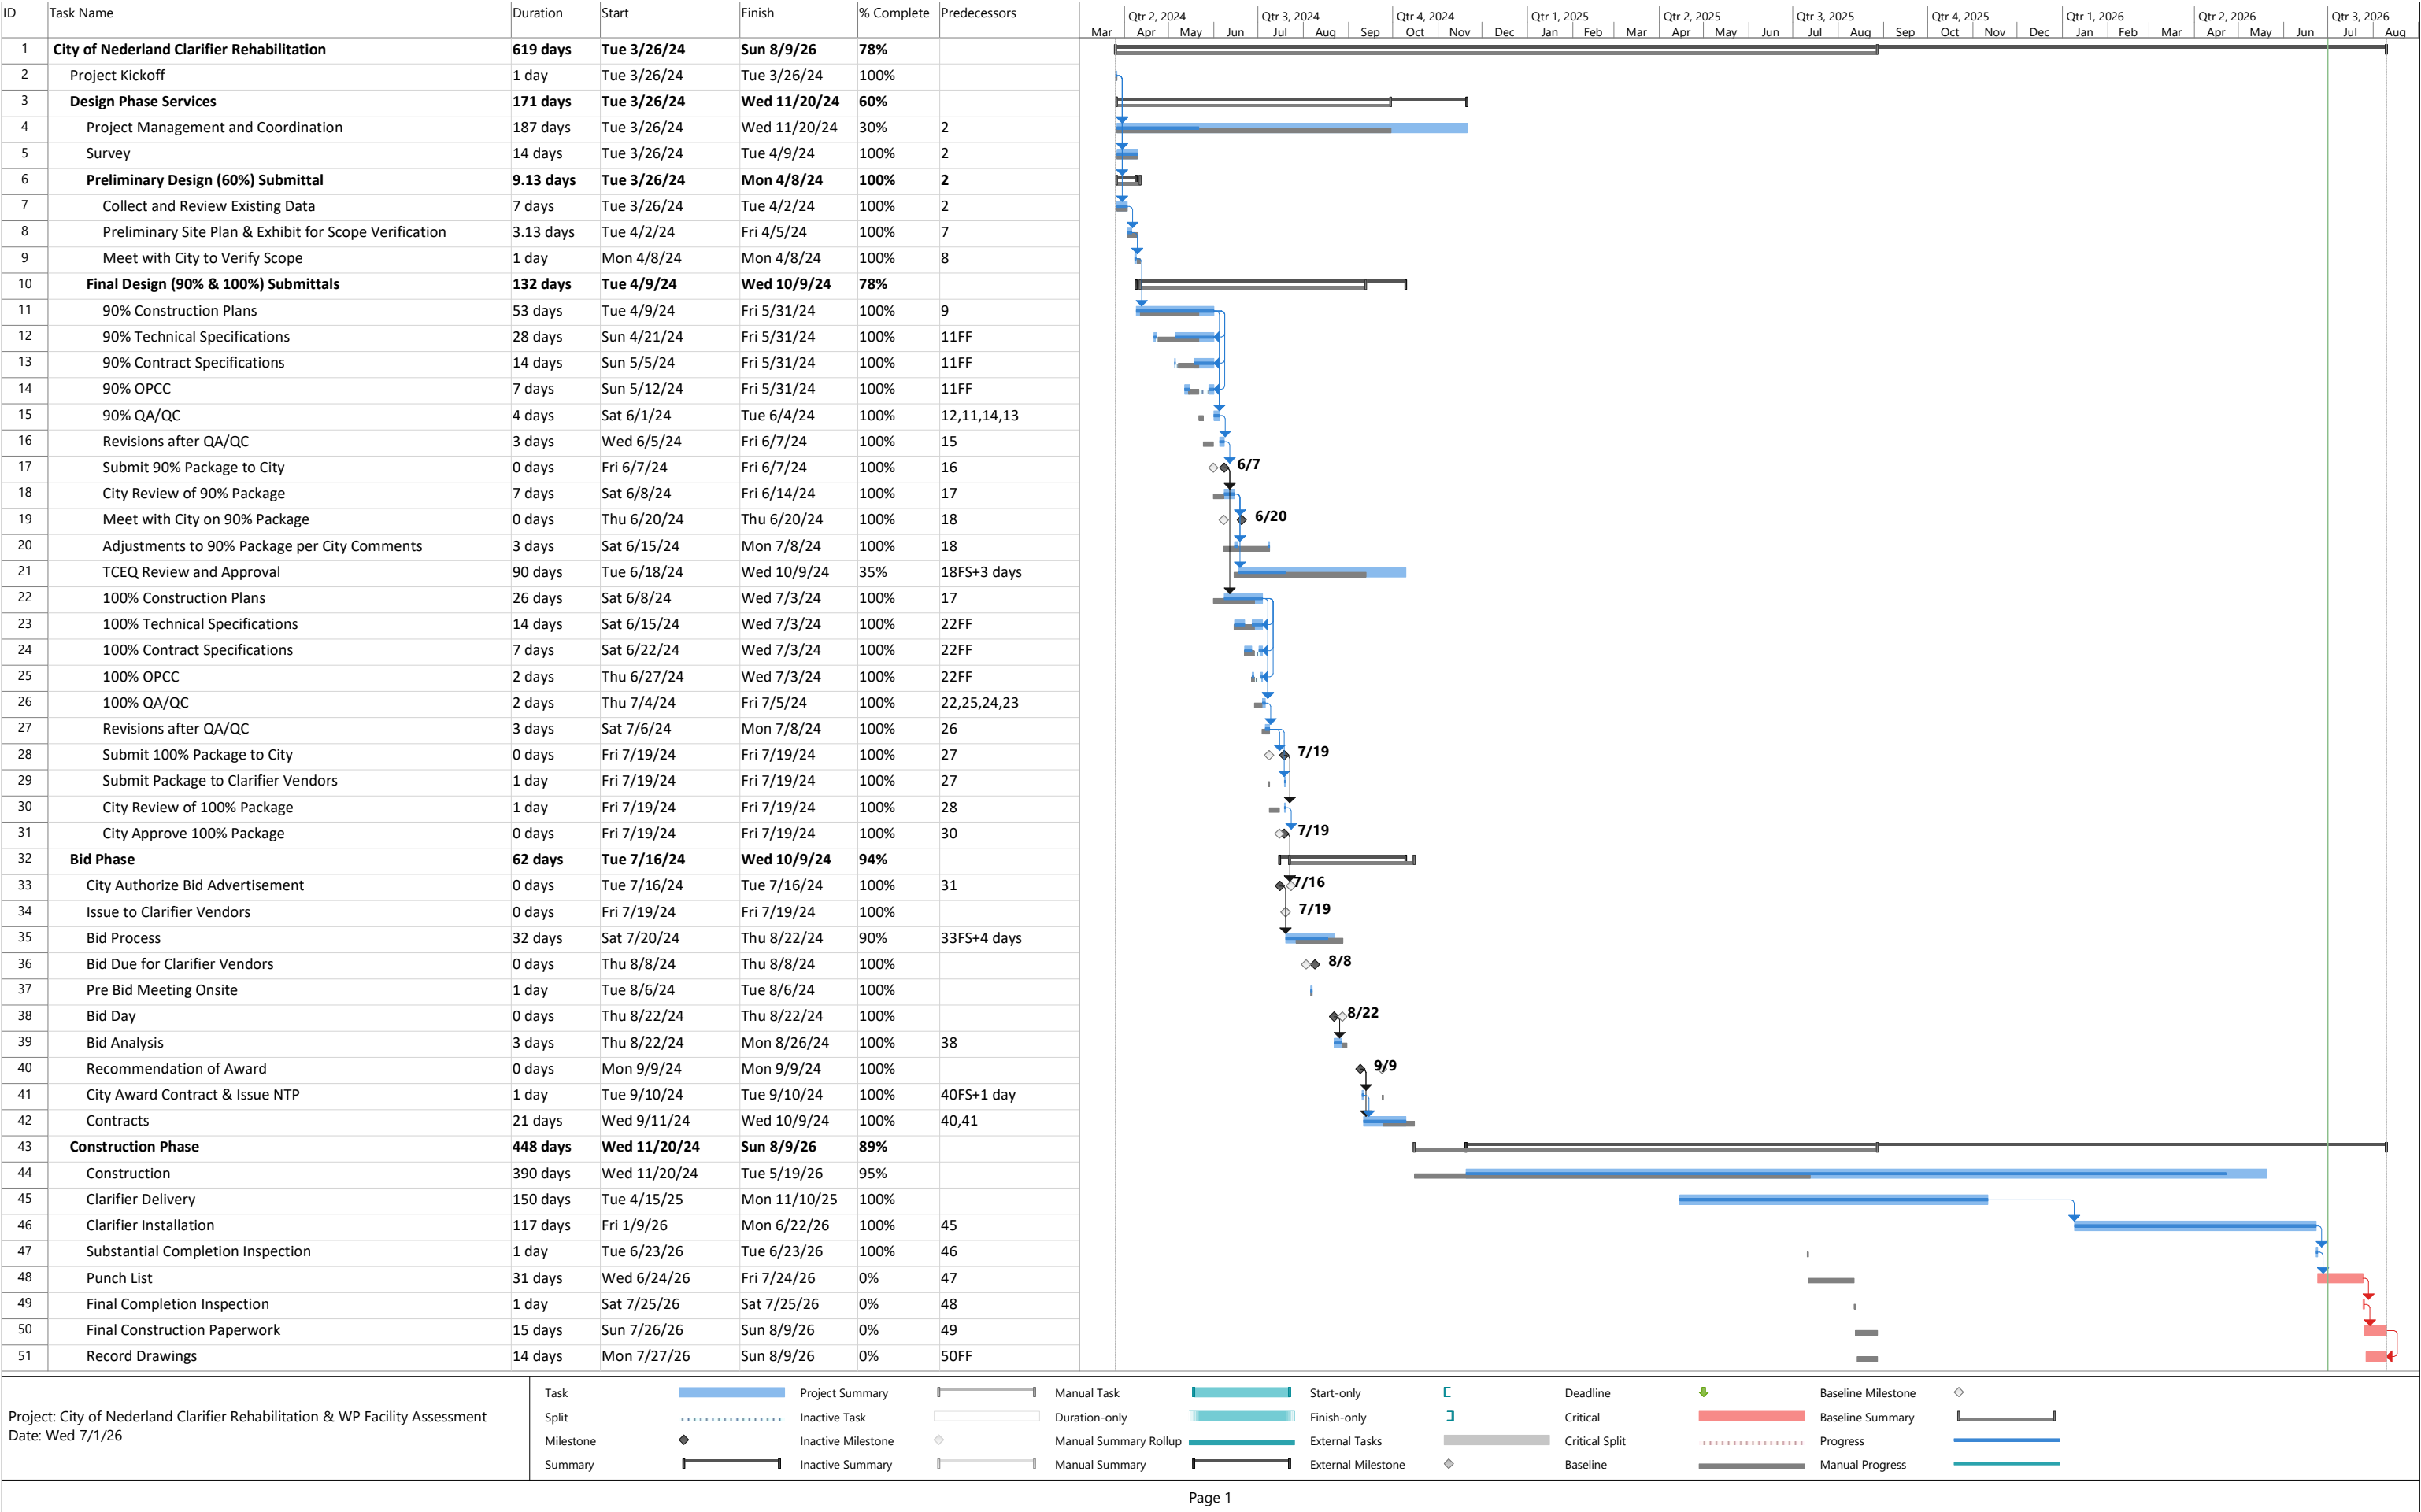

City of Nederland WWTP Centrifuge Replacement

Client Name: City of Nederland

Subject: Progress Report

Created By: Gabriela Y. Porras, PE

Westwood No.: R0043842.03

Date: 7/1/2026

Westwood

Work in Progress:

- With information from site visit, electrical and structural subconsultants are actively working on plan pages and cost estimates for related work.
- Sludge sampling and recommendation was completed.
- Coordination with Penn Valley Pump is completed regarding existing sludge metering pumps.
- Coordination with El2 and Alfa Laval to update their provided specification and plan sheets for centrifuge mounted on skid with diverter gate and polymer equipment. This is needed for procurement processes. Discussion regarding location of centrate chute on drawing as well as possibilities for getting the machine into the dewatering room.
- Pricing received from equipment suppliers. Research against previously bid similar projects in the area to evaluate various constructability options. Coordination with structural for evaluating suitability of existing structural systems (I-beams and hoist) for getting items in/out of dewatering room.

Work to be completed by next Progress Report:

- Confirm structural and electrical layouts in dewatering room with feedback from equipment vendor and subconsultants.
- Have the information for manufacturer finalized to begin procurement process.

Updates to the Schedule:

- The schedule shows coordination with manufacturer to be completed mid-June. This was a bit delayed due to staff vacations at Alfa Laval and finding a solution for the issue of the solids discharge chute being too close to a column. Though a meeting was held with Alfa Laval recently (6/29) to discuss what has been provided and what is needed from them finalize this information for procurement.

Project Notes / Questions:

- Is there anything else the City will require besides plans and specs for procurement?



City of Nederland WWTP Facility Assessment

Client Name: City of Nederland

Subject: Progress Report

Created By: Simone King, PE

Westwood No.: R0043842.04

Date: 7/1/2026

Westwood

Work in Progress:

- Westwood met with the City of Nederland to present observations of the existing wastewater treatment facility and discuss preliminary rehabilitation recommendations. The purpose of this meeting was to provide an update on project progress and confirm alignment with the City's expectations. Feedback from this meeting will be incorporated into the final Facility Assessment report.
- Coordination with equipment suppliers and manufacturers to obtain budgetary pricing for proposed improvements is ongoing. Budgetary pricing quotes will be used to support the development of preliminary construction cost estimates included in the assessment.
- Westwood continues to develop the Facility Assessment report, including documentation of existing conditions and performance, recommendations, cost estimates, permit considerations, and project phasing. The Facility Assessment is on track to be submitted for the City's review early-August.

Work to be completed by next Progress Report:

- Continued coordination with equipment suppliers and manufacturers to confirm and refine budgetary pricing.
- Continued development of the Facility Assessment report, including existing conditions and performance evaluation, photo documentation, recommendations, cost estimates, permit considerations, and project phasing.

Updates to the Schedule:

- Delays have been encountered with receiving budgetary pricing from the equipment vendors for various reason but expect to get information necessary in July.

Project Notes / Questions:

- City of Nederland WWTP operations staff to provide a site plan identifying requested lighting locations.

City of Nederland Lift Station Rehab

Client Name: City of Nederland

Subject: Progress Report

Created By: Jim Roberts, PE

Westwood No. R0043731.00

Date: 7/1/2026

Westwood

Work in Progress:

- 6/23/26. Met with Public Works staff to go over plans for 60% Canal Ave, 30% Nederland Ave.
- Upgrade pumps per discussion with Ned PW.
- 90% plans for Canal LS, 60% for Nederland LS.

Work to be completed by next Progress Report:

- 60% design of Canal Ave lift station. Keep existing wet well.
- 30% design plans for Nederland Ave lift station.
- Cleaning and Inspection of both lift station wet wells. Coordinate w/City.

Updates to the Schedule:

- No changes to schedule below.

Project Notes / Questions:

- Need confirmation of FM discharge location/length for Canal Ave forcemain.

SCHEDULE

Activity - Each Lift Station	Estimated Completion
Notice-To-Proceed	2/6/2026
Site Visit & Coord Survey & SUE	2/11/2026
Topo Survey	3/11/2026
Conceptual Design Submittal - After Survey (30%)	5/15/2026
City Review (30%)	5/29/2026
Preliminary Design Submittal (60%)	6/26/2026
City Review (60%)	7/10/2026
Bid Ready Submittal (90%)	8/7/2026
Final Client Review Complete	8/21/2026
Final Plans Complete (100%)	9/4/2026
Bidding & Award	10/30/2026
Begin Construction w/NTP	11/6/2026
Complete Construction (Estimate, per Station)	5/7/2027
Record Drawings	5/21/2027

City of Nederland Wastewater Rehab West

Client Name: City of Nederland

Subject: Progress Report

Created By: Jim Roberts, PE

Westwood No. R0069501.00

Date: 7/1/2026

Westwood

Work in Progress:

- 6/23/26 Met with Public Works staff to go over plans for Phase 1.
- Ordered AI reports to expedite pipeline video review and plans.
- Completing review of available Phase 2 video with AI reports.
- Received contact info from City for access to 6-7 remaining lots w/manholes.

Work to be completed by next Progress Report:

- Continue work on Phase 1 plans to 90% per schedule. Westwood will proceed with plans unless instructed otherwise by City pending SPI hydraulic analysis.
- Review 50% of Phase 2 video and recommendations with City.
- Finalize videos of remaining lines.

Updates to the Schedule:

- See schedule below.
- Phase 2 60% Design submittal pushed to 8/4, delay of 6 weeks due to variability of pipe materials and video interpretation.
- The Phase 1 plans will hold at 90% pending decision on SPI hydraulic analysis.

Project Notes / Questions:

- Some lines blocked by debris, couldn't complete video. AIMS to provide estimate for additional time to clear lines.

SCHEDULE

Activity	PHASE 1	PHASE 2 NORTH		PHASE 2 SOUTH
Kick-off Meeting	2/11/2026			
Clean & Televiser Lines - Part 1	3/1/2026			
Review Video w/Client - Part 1	4/7/2026	4/7/2026		
Clean & Televiser Lines - Part 2, Begin Design		3/15/2026		
Review Video w/Client - Part 2		4/14/2026		
Clean & Televiser Lines - Part 3		5/12/2026		
Review Video w/Client - Part 3		5/26/2026		
Design - 60% Plans	6/23/2026	8/4/2026		9/4/2026
City Review - 60% Plans	7/7/2026	8/18/2026		9/18/2026
Design - 90% Plans	8/4/2026	9/15/2026		10/15/2026
City Review - 90% Plans	8/18/2026	9/29/2026		10/29/2026
Design - 100% Plans	9/15/2026	10/16/2026		11/16/2026
City Review - 100% Plans	9/29/2026	10/30/2026		11/30/2026
Bidding	11/24/2026	1/30/2027		1/30/2027
Construction	11/23/2027	1/30/2028		1/30/2028

City of Nederland Water Plant Clarifier #2

Client Name: City of Nederland

Subject: Progress Report

Created By: Kris Glende

Westwood No.: R0043842.02

Date: 7/9/2026

Westwood

Work in Progress:

- Survey is scheduled to visit site the week of July 13th.
- Design team is working to setup drawings and move project forward
- Coordination with electrical & structural subconsultant in progress.

Work to be completed by next Progress Report:

- Engagement with ClearStream for Clarifier procurement package will be initiated ASAP
- Preliminary project plan for Operator review and agreement

Updates to the Schedule:

- Schedule needs to be updated

Project Notes / Questions:

- None at this time.

City of Nederland Water Plant Chemical Feed Station Improvements

Client Name: City of Nederland

Subject: Progress Report

Created By: Kris Glende

Westwood No.: R0043842.07

Date: 7/9/2026

Westwood

Work in Progress:

- Survey is scheduled to visit site the week of July 13th.
- Design team is working to setup drawings and move project forward
- Coordination with electrical & structural subconsultant in progress.

Work to be completed by next Progress Report:

- Engagement with Moody Bros and EI2 for comparable chem feed equipment will be initiated ASAP
- Engagement with Chemical Tank Manufacturers will be initiated ASAP
- Piping arrangement and operational improvements to be evaluated and determined

Updates to the Schedule:

- Schedule needs to be updated

Project Notes / Questions:

- None at this time.

City of Nederland Water Plant Filter Replacement

Client Name: City of Nederland

Subject: Progress Report

Created By: Kris Glende

Westwood No.: R0043842.05

Date: 7/9/2026

Westwood

Work in Progress:

- Survey is scheduled to visit site the week of July 13th.
- Design team is working to setup drawings and move project forward
- Coordination with electrical & structural subconsultant in progress.

Work to be completed by next Progress Report:

- Engagement with Ovivo for Filter equipment design information will be initiated ASAP
- Engagement with valve and actuator vendors will be initiated ASAP
- Preliminary project plan for Operator review and agreement
- Draft construction sequencing will be prepared and reviewed with Operator

Updates to the Schedule:

- Schedule needs to be updated

Project Notes / Questions:

- None at this time.
