

City of Nederland WWTP Facility Assessment

Client Name: City of Nederland

Subject: Progress Report

Created By: Simone King, PE

Westwood No.: R0043842.04

Date: 5/5/2026

Westwood

Work in Progress:

- The project team is performing the condition assessment of the WWTF and delineating preliminary rehabilitation recommendations to be discussed with the City prior to finalizing the assessment report.

Work to be completed by next Progress Report:

- Electrical subconsultant to complete initial field reconnaissance/site visit.


Updates to the Schedule:

- No major updates, expect to schedule a meeting to review preliminary recommendations with City in mid to late May.

Project Notes / Questions:

- None at this time.

ID	Task Name	Duration	Start	Finish	% Complete
1	City of Nederland Wastewater Treatment Plant Facility Assessment	Working Days	Thu 1/15/26	Mon 7/6/26	16%
2	Facility Assessment	147 days?	Thu 1/15/26	Fri 8/7/26	16%
3	Notice to Proceed	1 day	Thu 1/15/26	Thu 1/15/26	100%
4	Project Site Visit	1 day	Thu 3/5/26	Thu 3/5/26	100%
5	Data Collection	6 days	Fri 3/6/26	Fri 3/13/26	90%
6	Review of Existing WWTP Records	15 days	Mon 3/16/26	Fri 4/3/26	80%
7	Condition Assessment of Existing Facilities	15 days	Mon 3/16/26	Fri 4/3/26	20%
8	Electrical Subconsultant Site Visit	1 day?	Fri 3/27/26	Fri 3/27/26	0%
9	Electrical Design Coordination Meeting	1 day	Mon 4/6/26	Mon 4/6/26	0%
10	Initial Development of Rehabilitation Recommendations & Project List	30 days	Mon 4/6/26	Fri 5/15/26	23%
11	Develop rehabilitaiton recommendations and identify projects	25 days	Mon 4/6/26	Fri 5/8/26	25%
12	Exhibit Preparation	5 days	Mon 5/11/26	Fri 5/15/26	10%
13	Equipment Supplier Coordination	10 days	Mon 4/6/26	Fri 4/17/26	0%
14	Rehabilitation Recommendations & Project List Review with City	5 days	Mon 5/18/26	Fri 5/22/26	0%
15	Draft WWTP Facility Assessment	19 days	Mon 5/25/26	Thu 6/18/26	0%
16	Cover, Table of Contents, and Contact Information	9 days	Mon 5/25/26	Thu 6/4/26	0%
17	Executive Summary and Introduction	9 days	Mon 5/25/26	Thu 6/4/26	0%
18	Existing Condition Assessment	9 days	Mon 5/25/26	Thu 6/4/26	0%
19	Project Recommendations	9 days	Mon 5/25/26	Thu 6/4/26	0%
20	Project Cost Estimates	9 days	Mon 5/25/26	Thu 6/4/26	0%
21	CIP Development	9 days	Mon 5/25/26	Thu 6/4/26	0%
22	Exhibits & Appendices	10 days	Fri 6/5/26	Thu 6/18/26	0%
23	QA/QC	15 days	Fri 6/19/26	Thu 7/9/26	0%
24	Internal QA/QC	7 days	Fri 6/19/26	Mon 6/29/26	0%
25	Respond to Internal QA/QC Comments	8 days	Tue 6/30/26	Thu 7/9/26	0%
26	Submit Draft WWTP Facility Assessment to the City	1 day	Fri 7/10/26	Fri 7/10/26	0%
27	City Review of Facility Assessment	9 days	Mon 7/13/26	Thu 7/23/26	0%
28	WWTP Facility Assessment Review Meeting with the City	1 day	Fri 7/24/26	Fri 7/24/26	0%
29	Finalize WWTP Facility Assessment with City's feedback	9 days	Mon 7/27/26	Thu 8/6/26	0%
30	Finalize & Submit Final WWTP Facility Assessment to the City	1 day	Fri 8/7/26	Fri 8/7/26	0%

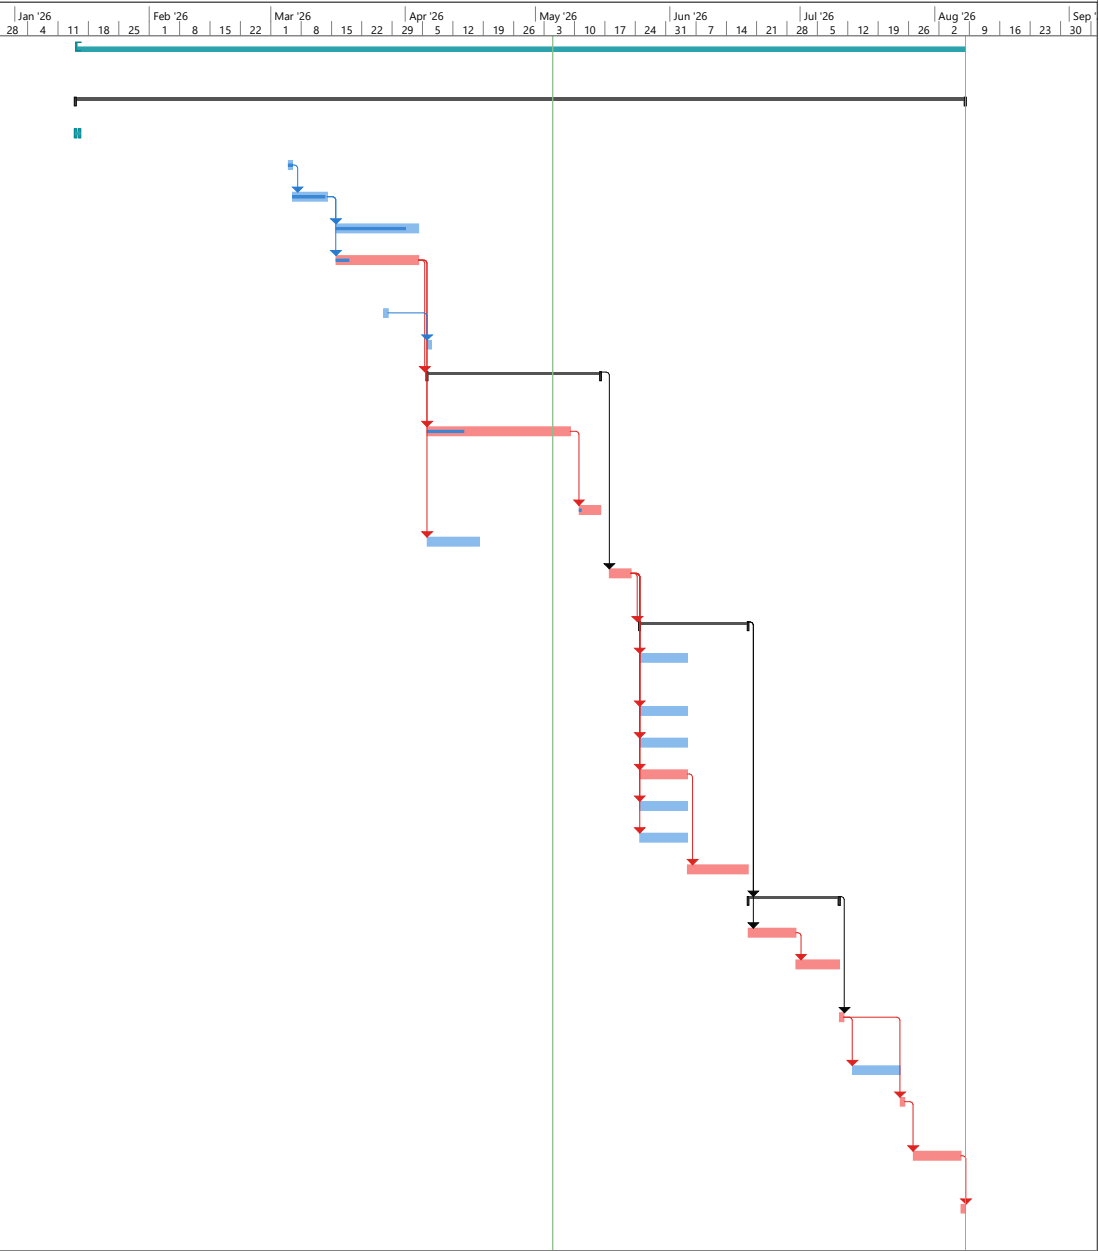

Westwood

Task	Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	Critical Split
Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	Progress
Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Critical	Manual Progress

City of Nederland WWTP Centrifuge Replacement

Client Name: City of Nederland

Subject: Progress Report

Created By: Gabriela Y. Porras, PE

Westwood No.: R0043842.03

Date: 5/5/2026

Westwood

Work in Progress:

- Preliminary plan pages were started using as-builts and survey information.
- Coordination with electrical and structural subconsultants is in progress.
- Coordination with EI2 and Alfa Laval to confirm centrifuge sizing, polymer equipment, and diverter gate recommendation.

Work to be completed by next Progress Report:

- Confirm structural and electrical layouts in dewatering room.
- Confirm location of polymer skids and piping to dewatering room.
- Possibly schedule a sludge sample as desired by Client.

Updates to the Schedule:

- No major updates. Meeting scheduled to review preliminary recommendations with City in mid to late May and move forward with Centrifuge procurement in June/July.

Project Notes / Questions:

- None at this time.

City of Nederland Water Plant Clarifier #1

Client Name: City of Nederland

Subject: Progress Report

Created By: Trey Glasper

Westwood No.: R0043842.00

Date: 5/5/2026

Westwood

Work in Progress:

- Sludge pit valves are on site, and the contractor will proceed with installation as weather permits. Once the valve is successfully installed, the clarifier will be filled.
- Contractor to fix minor sag in aerial bridge

Work to be completed by next Progress Report:

- WPS & Electrical subconsultant to complete substantial completion site visit
- Substantial completion inspection and punch list generation
- Request and receive final paperwork from Contractor

Updates to the Schedule:

- No updates

Project Notes / Questions:

- None at this time.

City of Nederland Lift Station Rehab

Client Name: City of Nederland

Subject: Progress Report

Created By: Jim Roberts, PE

Westwood No. 43731.00

Date: 5/5/2026

Westwood

Work in Progress:

- Coordinate with SPI for stations flow data/service area.
- System curve calculations. SPI to provide flow/service area data.
- Preliminary valve and forcemain layout

Work to be completed by next Progress Report:

- 30% design of Canal Ave lift station.
- Begin design of Nederland Ave lift station.

Updates to the Schedule:

- See attached schedule. 30% Design and City Review are pushed back two weeks. Should not impact Bidding schedule.

Project Notes / Questions:

- SPI agreed to provide stations flow data for pump design.

SCHEDULE

Activity - Each Lift Station	Estimated Completion
Notice-To-Proceed	2/6/2026
Site Visit & Coord Survey & SUE	2/11/2026
Topo Survey	3/11/2026
Conceptual Design Submittal - After Survey (30%)	5/15/2026
City Review (30%)	5/29/2026
Preliminary Design Submittal (60%)	6/26/2026
City Review (60%)	7/10/2026
Bid Ready Submittal (90%)	8/7/2026
Final Client Review Complete	8/21/2026
Final Plans Complete (100%)	9/4/2026
Bidding & Award	10/30/2026
Begin Construction w/NTP	11/6/2026
Complete Construction (Estimate, per Station)	5/7/2027
Record Drawings	5/21/2027

City of Nederland Wastewater Rehab West

Client Name: City of Nederland

Subject: Progress Report

Created By: Jim Roberts, PE

Westwood No. 69501.00

Date: 5/5/2026

Westwood

Work in Progress:

- Reviewed video on Phase 1 section. Very few blockages observed.

Phase 1 design waiting for SPI hydraulic study for potential upsizing.

- Continue to review video on Phase 2 area, north of Helena.
- AIMS to continue to video Phase 2 area.
- Street layout for Phase 2 section for design in progress.

Work to be completed by next Progress Report:

- Review Phase 1 results with City. Schedule date.
- Review Section of Phase 2 video with City.
- Coordinate with SPI on hydraulic analysis for Phase 1 section.
- Update schedule format.

Updates to the Schedule:

- See schedule below.
- The Phase 1 60% plans are on hold until we know results from SPI hydraulic

Project Notes / Questions:

- Need assistance from City for access to some homes who refused AIMS. Addresses to be provided.
- Some lines blocked by debris, couldn't complete video. AIMS to provide

SCHEDULE

Activity	PHASE 1	PHASE 2
Kick-off Meeting	2/11/2026	
Clean & Televise Lines - Part 1	3/1/2026	
Review Video w/Client - Part 1	4/7/2026	4/7/2026
Clean & Televise Lines - Part 2, Begin Design		3/15/2026
Review Video w/Client - Part 2		4/14/2026
Clean & Televise Lines - Part 3		5/12/2026
Review Video w/Client - Part 3		5/26/2026
Design - 60% Plans	On Hold	6/9/2026
City Review - 60% Plans	5/19/2026	6/23/2026
Design - 90% Plans	6/30/2026	8/4/2026
City Review - 90% Plans	7/14/2026	8/18/2026
Design - 100% Plans	8/11/2026	9/15/2026
City Review - 100% Plans	8/25/2026	9/29/2026
<i>Bidding</i>	10/20/2026	11/24/2026
<i>Construction</i>	2/9/2027	11/23/2027
